




## Rose/Grove Reconstruction Project Project Update, September 23, 2021

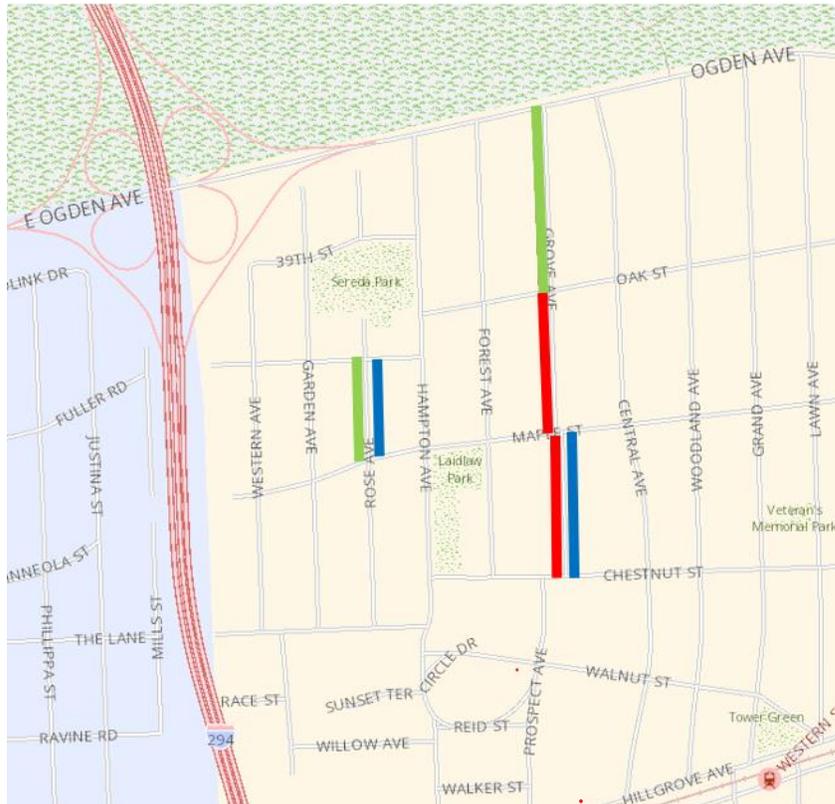

- Water main installation – expected to start and be completed in 2021
- Road reconstruction – expected to start and be substantially completed in 2021
- Road reconstruction – expected to start Spring 2022 and be completed Summer 2022

Dear resident:

Thank you for your continued patience as you await the start of the much-needed infrastructure improvements on Rose and Grove Avenues. Due to IEPA Loan processing delays and contractor scheduling issues the project has not yet started. As a result of the delays, it is no longer feasible to complete the entire project this calendar year. This month Village Staff and the consultant project engineer have been working with the contractor, A Lamp Concrete Contractors, to develop an updated project schedule. The schedule for each block is slightly different as illustrated on the map. Preliminary work and mobilization has already begun. We anticipate water main installation work starting the week of 9/27.

(over)

**PRESIDENT**

Alice Gallagher

**TRUSTEES**

Heidi Rudolph

James Tyrrell

Nicole Chen

Alan Fink

James John

Scott Lewis

**CLERK**

Edward Tymick

**ACTING VILLAGE  
MANAGER**

Casey Biernacki

**DIRECTORS**

Grace Turi

Pat Schramm

Martin Scott

Matthew Supert

Brian Budds

Ellen Baer

Aleks Briedis

Michael Kelly

Jefferey Koza

**Project Schedule – Grove, Chestnut to Maple:**

The contractor (A Lamp Concrete Contractors) as of the date of this letter expects to start water main installation work on Grove Ave from Chestnut Street to Maple Street the week of 9/27. The water main work is expected to take 3-4 weeks to complete. Once the new water main and water services have been installed the contractor will begin roadway reconstruction. The Village is expecting to have road reconstruction work on Grove, Chestnut to Oak, substantially completed by the end of November.

**Project Schedule – Grove, Maple to Oak:**

Sewer repairs at select locations will be performed next month. The road reconstruction on this block is expected to start in 3-4 weeks. The contractor must first complete water main installation work on Grove between Maple and Chestnut. The Village is expecting to have road reconstruction work on Grove, Chestnut to Oak, substantially completed by the end of November.

**Project Schedule – Grove, Oak to Ogdan:**

It is currently anticipated that work on this block will begin Spring 2022. There may be sewer repairs or other minor work completed this year however the road reconstruction work is not expected to begin until Spring 2022. We currently anticipate the road reconstruction will be completed by Summer 2022.

**Project Schedule – Rose, Maple to Oak:**

We anticipate water main installation work will begin in October on this block. This work is expected to take 3-4 weeks to complete. The contractor expects to complete the installation of the new water main and water service lines this year. The utility trenches in the pavement will be patched with asphalt this year and the road reconstruction work will begin in Spring and be completed by Summer 2022.

**Stay Informed**

Please visit the project website [www.wsprings.com/rosegrove](http://www.wsprings.com/rosegrove) and click on “Stay Informed” on the left side of the web page to sign up for project updates for this project.

**Project Contacts**

The Village is utilizing Baxter & Woodman, an engineering consultant firm, to handle construction inspection of the project. During construction should you have any immediate construction related issues please contact the project’s resident engineer Patrick O’Donoghue at 847-848-0543 or via email at [podonoghue@baxterwoodman.com](mailto:podonoghue@baxterwoodman.com).

The Village’s Engineering Services Department is responsible for overall project management and oversight of the project. Any general project questions can be directed to Village Engineer Jeff Koza, PE at 708-246-1800 ext 202 or email [jkoza@wsprings.com](mailto:jkoza@wsprings.com).
